



Three T
Interreg Europe



European Union
European Regional
Development Fund

ThreeT Thematic Trail Trigger PHASE 2

Carlos Carrillo

Transportes Interurbanos de Tenerife
international@titsa.com

Action Plan Progress

Actions as indicated in the partner AP	Corresponding activities executed in the last 3 months	By whom	Deliverables	Estimated % of progress advancement
<p>Modified buses to carry surfboards</p>	<p>Closing the bidding process and analysis and evaluation of the technical proposals received</p>	<p>TITSA</p>	<p>Selection and signing of the contract with the winning company</p>	<p>100%</p>
	<p>Preparation of the technical report of the offers received</p>	<p>TITSA</p>	<p>Selection and signing of the contract with the winning company</p>	<p>100%</p>
<p>Tourist Passport</p>	<p>Design of a trail plan for its inclusion into titsa's app and website</p>	<p>TITSA/GUIAN ATURA</p>	<p>Selection of trails that connect with titsa routes and design of the interactive map as well as all the relevant information about it to be included in the TITSA web application.</p>	<p>75%</p>



Meetings and other relatable events held in the period

ST meeting/ other event during the quarter	Date	Place	N° of participants	Content
Follow-up meeting (trails)	13/05/2022	TITSA's office	5	Meeting with the winner of the minor contract for the design of the trails and all the information to be included in the titsa web application to view the progress of the development project and estimate a completion date for the work
Follow-up meeting (trails)	08/06/2022	TITSA's office	5	Meeting to assess the estimated delay of the company contracted to prepare trail maps and find possible solutions with the idea of having everything ready to start using it on the web on August 1.
Follow-up meeting (trails)	30/06/2022	TITSA's office	5	Given the delay accumulated by the contracted company, this meeting is held to set a new possible implementation date for the information and maps of the trails on the web and the app.
Follow-up meeting (trails)	28/07/2022	TITSA's office	5	New meeting with the documentation received and prepared by the external company to check the quality of the work and agree on the hiring of other companies for the graphic design of the maps to be inserted on the web and app. Meanwhile, it is agreed to prepare an informative tab on the TITSA website that will serve as information for what will be introduced soon.


Possible options for the tourist passport





Trails with TITSA

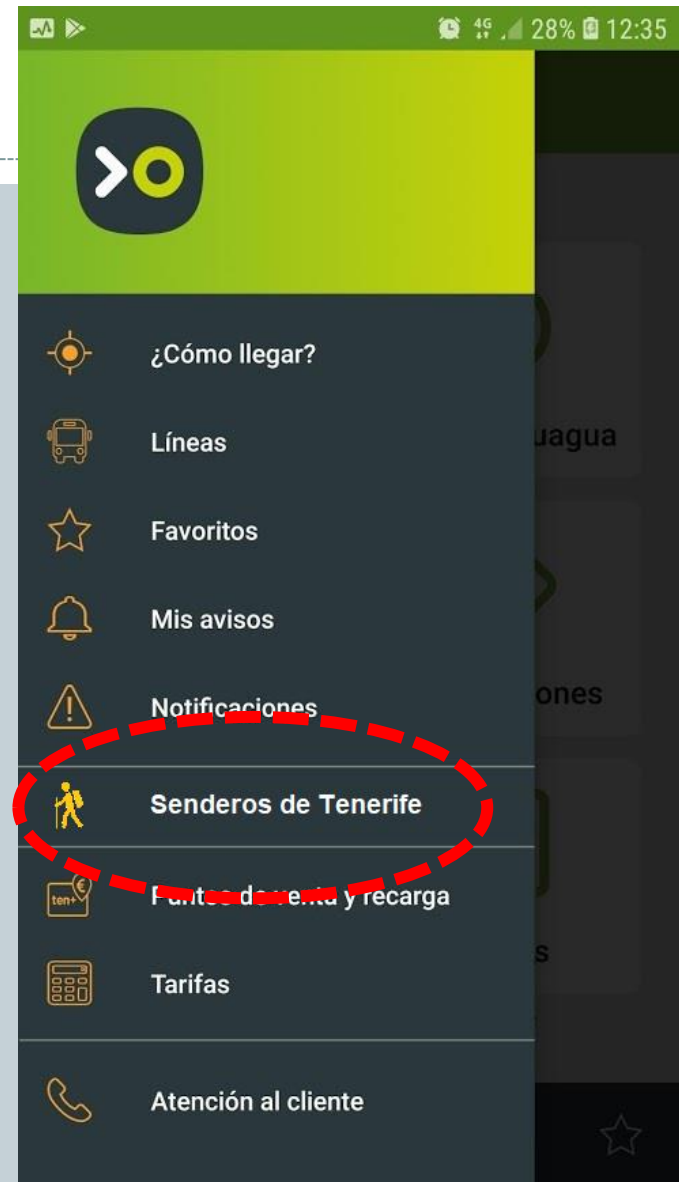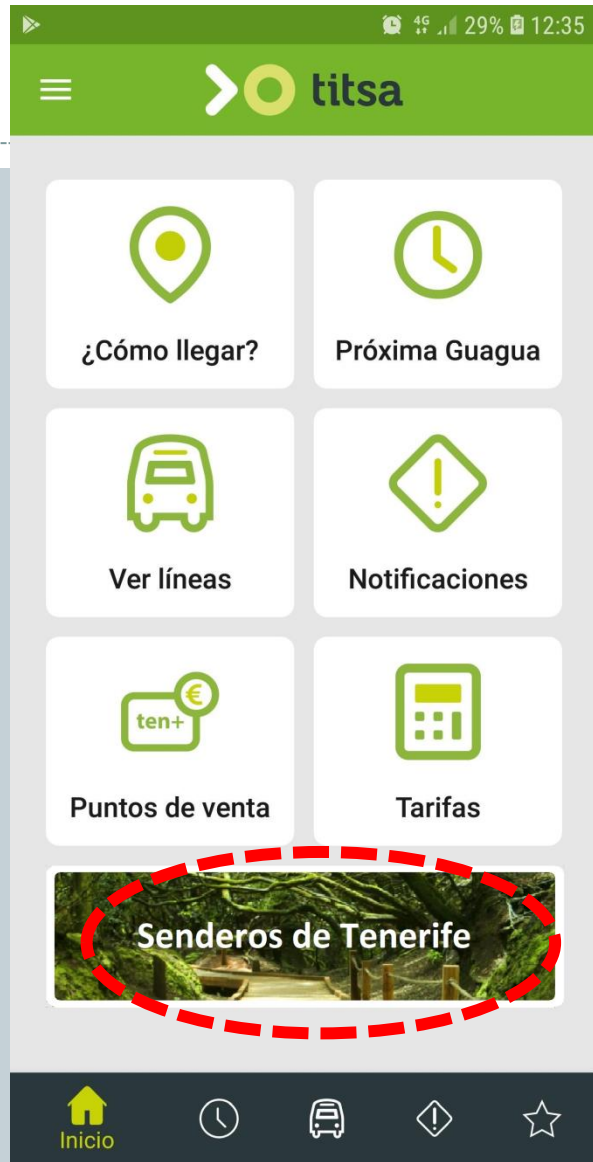

Development in 3 main areas

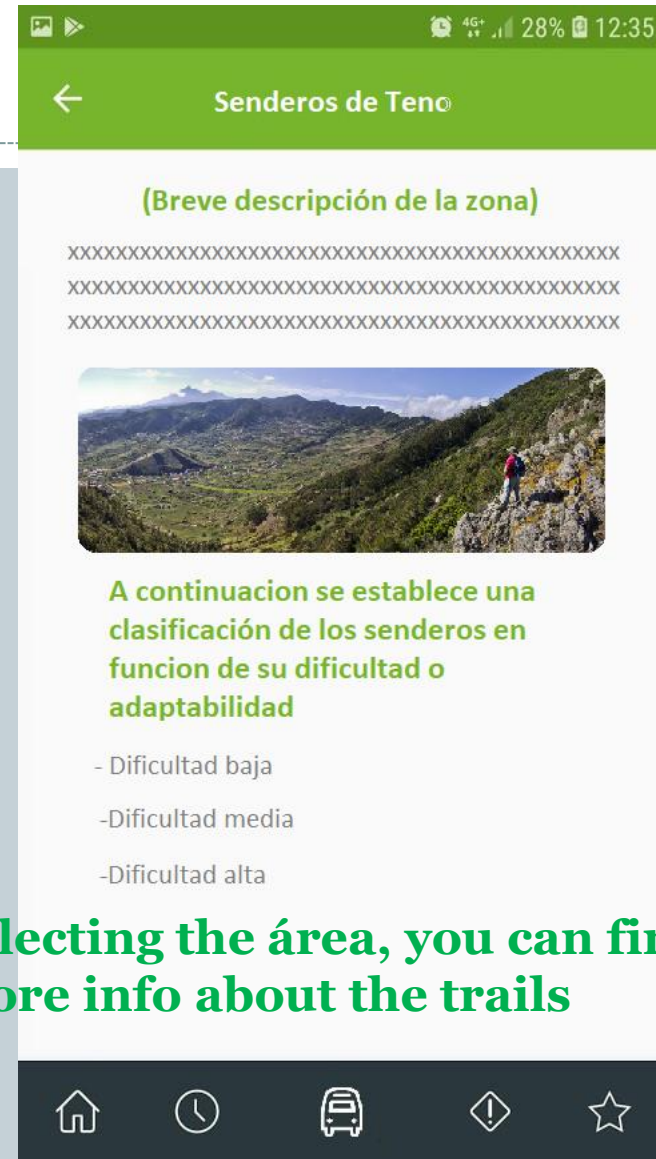


Selecting the área, you can find more info about the trails

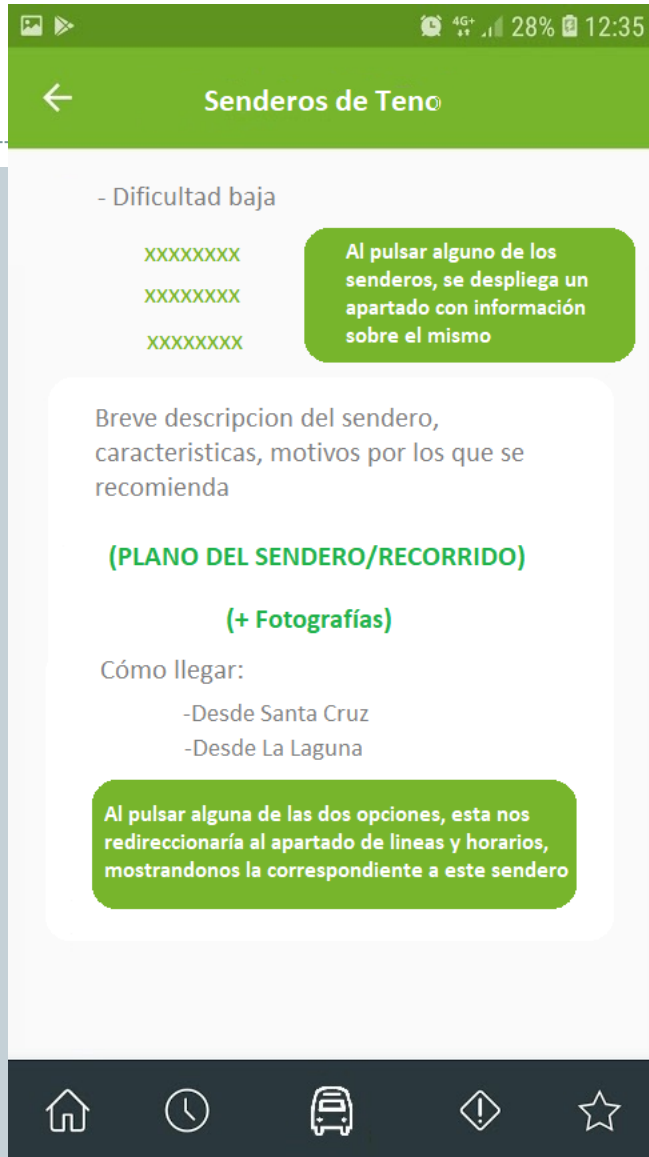

Selecting the area, you can find more info about the trails


Identified trails and routes

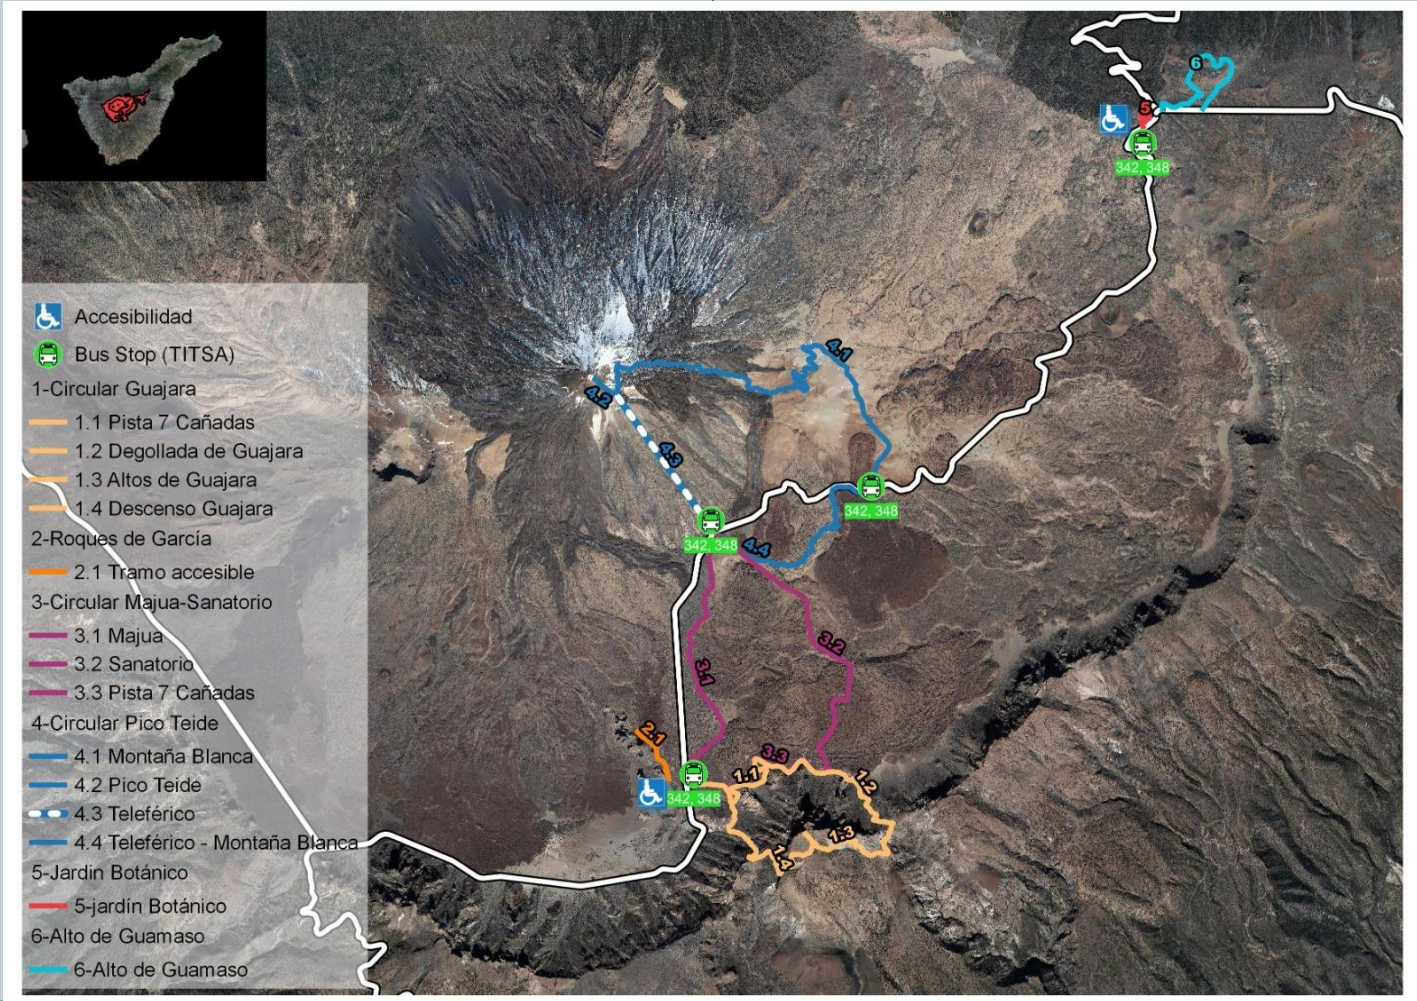


Now in our web



INICIO TITSA TUS GUAGUAS TENERIFE EN GUAGUA ATENCIÓN AL CLIENTE TITSA CONECTA TRANSPARENCIA Empleados



titisa
donde tú vas




ESTE VERANITO
AL GUAGUA PATOS

INICIO / Tenerife en Guagua


Tenerife en Guagua

>


Ofrecemos cobertura integral a los servicios de transporte por carretera de Tenerife.




AEROPUERTO TENERIFE NORTE.
Conoce todas las líneas que te llevan al Aeropuerto de Los Rodeos (TFN).




AEROPUERTO TENERIFE SUR.
Conoce todas las líneas que te llevan al Aeropuerto Reina Sofía (TFS).



LÍNEAS TURÍSTICAS DE TENERIFE.
Plano interactivo de Tenerife con nuestras líneas turísticas.



LÍNEAS TURÍSTICAS DE SANTA CRUZ.
Plano interactivo de Santa Cruz con nuestras líneas turísticas.



TENERIFE EN GUAGUA.
Conoce los senderos a los que puedes llegar en guagua.

Atención al Cliente: **922 531 300** (08:00h - 20:00h)

Modified Buses




Trails with TITSA

The Bus modified to carry surfboards



TITSA has acquired new modified buses to take surfboards to coastal areas where there are also nearby trails, trying to encourage the use of public transport.

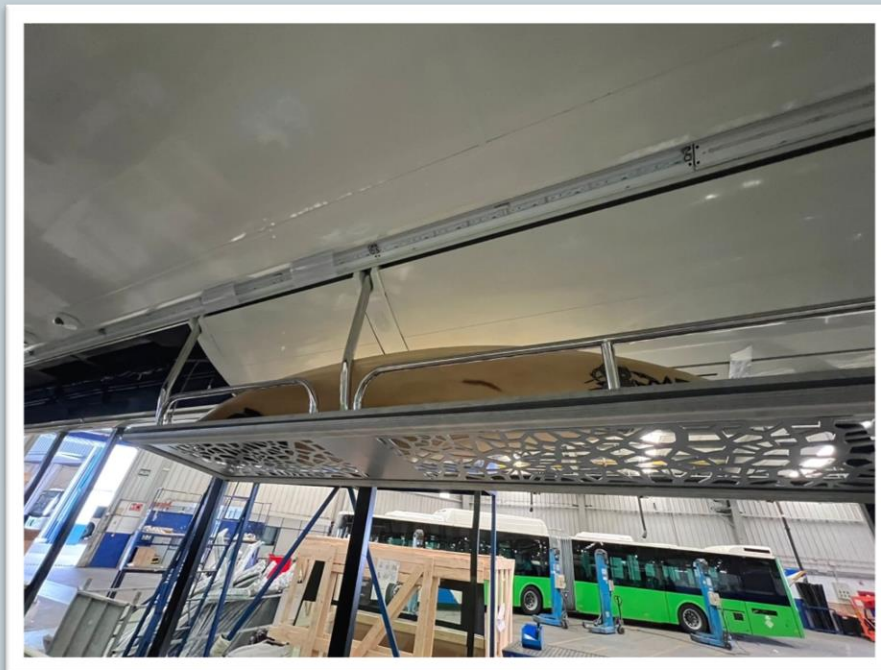

The objective:



AVOID THIS!

